

# Snowcreek Development Agreement - 2017 Annual Review Report

## Development Agreement Schedule of Performance Review

### Snowcreek Hilltop Development Company, L.P. & Snowcreek Investment Company, L.P. Development Agreement

#### Summary: Snowcreek Development Agreement

**Effective Date:** July 23, 2010

**Term:** 20 years


**Expiration Date:** July 23, 2030

#### Affected Projects:


1. Snowcreek VII
2. Snowcreek VIII

**Town Manager Determination:** Developer is found to be in good faith substantial compliance with the terms and conditions of the Snowcreek Development Agreement.

**Town Manager:** Daniel C. Holler

**Signature:** 

**Date:** December 6, 2017

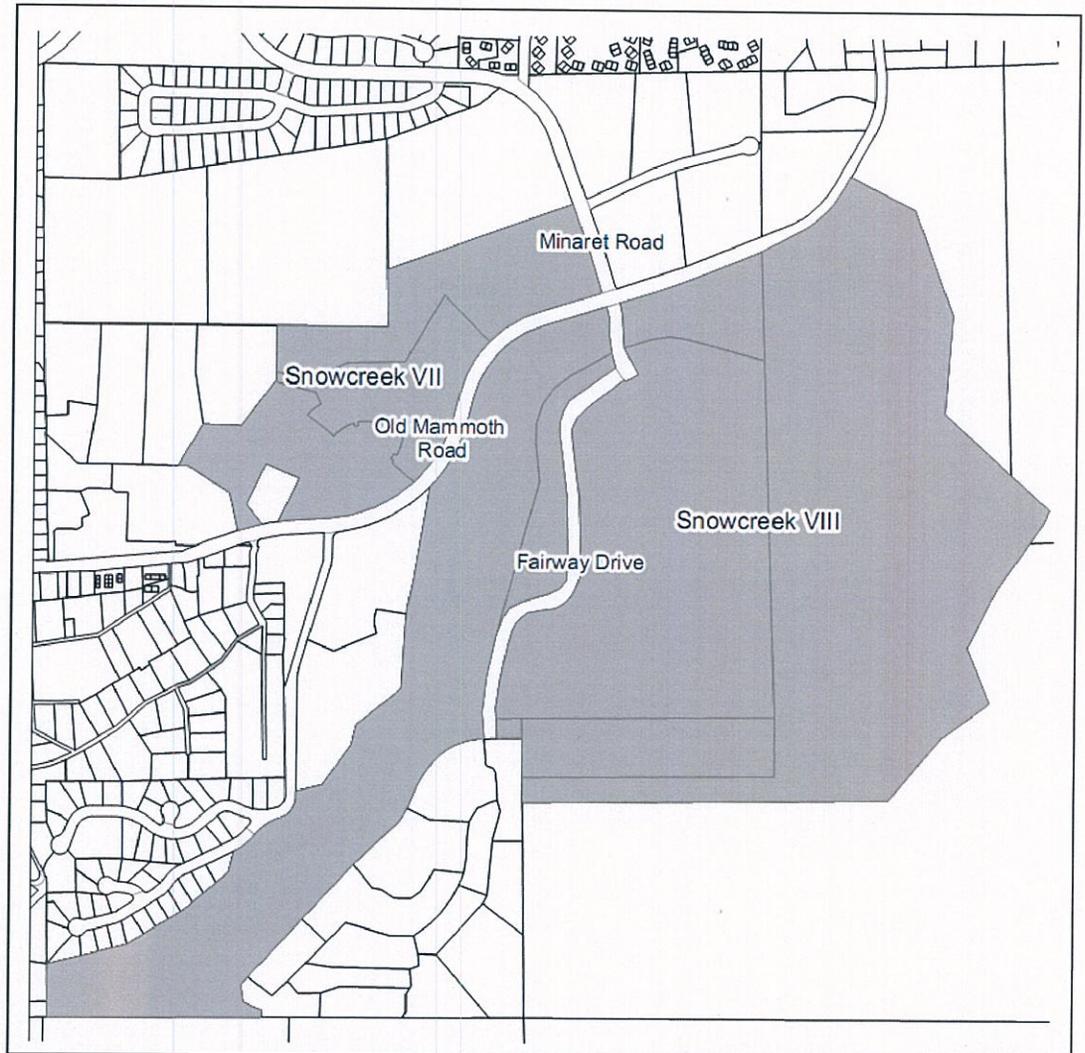

## Snowcreek Development Agreement – 2017 Annual Review Report

### Development Agreement Milestones (Article 2, Section 2.2.1)

Subject	Milestone	Due Date	Actual Date of Implementation	Satisfied/Complete	Notes
Annual Review	Developer will initiate the annual review by submitting a written statement to the Town Manager describing the Developer's good faith substantial compliance with the terms and conditions of the DA for the prior calendar year (7.2.2).	Initiated October 31 <sup>st</sup> each year	Letter dated October 26, 2017	Yes	This annual review report is to be received and filed by Town Council on December 6, 2017.
Backcountry Egress	Allow egress of backcountry skiers, snowboarders, and snowshoers from the Sherwin Range prior to effective date of DA (2.2.1.a).	Prior to effective date of DA	Prior to effective date of DA	Yes	
	Continue to allow [egress of backcountry skiers, snowboarders, and snowshoers from the Sherwin Range] during the pendency of construction of that portion of the Projects so long as the Developer, at its sole election, determines that such egress shall not negatively affect public safety (2.2.1.a).	On-going during construction of portion of the Projects that would affect that Sherwin Range egress			
Mammoth Creek Open Space Corridor	Record a real estate conveyance document, whether a grant deed, a conservation easement, or another legal mechanism reasonably approved by the Town Attorney, to permanently protect the Mammoth Creek Open Space Corridor (2.2.1.b).	July 23, 2014			The Developer has been coordinating with DFW and the Town to donate the property to the Town by grant deed along with a third party conservation easement to DFW. The Town Council accepted the donation of the property and

**Snowcreek Development Agreement – 2017 Annual Review Report**

				<p>authorized the Town Manager to sign the grant deed on May 18, 2016 and the Town has been working with DFW to draft the conservation easement and the required Land Management Plan (LMP). The DFW Conservation Board is scheduled to consider the acceptance of the conservation easement on November 30<sup>th</sup>. Since the DFW process is outside of the Developer's control, the Town has determined that the Developer is in good faith substantial compliance with the Snowcreek DA.</p>
--	--	--	--	--

**Snowcreek Development Agreement – 2017 Annual Review Report**

Phasing	Actual construction will occur in phases and subphases based on what the market will absorb at any given point in time. It is the intention of the parties for each phase or subphase of the Projects to provide all of the facilities, programs (including affordable housing), features, amenities, access and easements described in the Vested Rules as well as payment of all fees at the time set forth in the Vested Rules, related to that phase or subphase. The parties agree to discuss the actual phasing of development and the associated timing for completion of facilities, programs (including affordable housing), features, amenities, access and easements in connection with the application for each use permit or Subsequent Approval (2.2.1.c.1).	Application for each use permit or Subsequent Approval; on-going with each phase of construction			
Resort Hotel and 18-Hole Golf Course	Subject to Section 11.15, if development of the Resort Hotel and 18-hole championship golf course has not commenced within 10 years after the effective date of the DA, then the remaining 10-year term of the DA shall be reduced one day for each day, or portion thereof, the 10-year milestone has not been met (2.2.1.c.2).	July 23, 2020			
Project Sales Price	Publicly available Project sales price activity shall be reviewed during the Annual Review, pursuant to Section 7.2 (2.2.2.f.3)	During annual review once units are for sale or have been sold			

---

## **Snowcreek Development Agreement – 2017 Annual Review Report**

### **Additional Progress**

In addition to the milestones identified above, progress has been made on Snowcreek permits:

- The first of four multi-unit buildings at Creekhouse (Snowcreek VII) is expected to be completed in January 2018. The other three buildings are all under construction.
- The golf course recycled water pond project was completed in summer 2015 and has been connected to the MCWD recycled water system.
